


CIVIC TECH KW / WR

Affordable Housing Portal: Second Season

The first season created the foundation. The second season turns it into a usable service that stakeholders can review, deploy, and put into real workflow.

Pilot-ready

16 weeks of feedback-led development, deployment hardening, and stakeholder handoff.

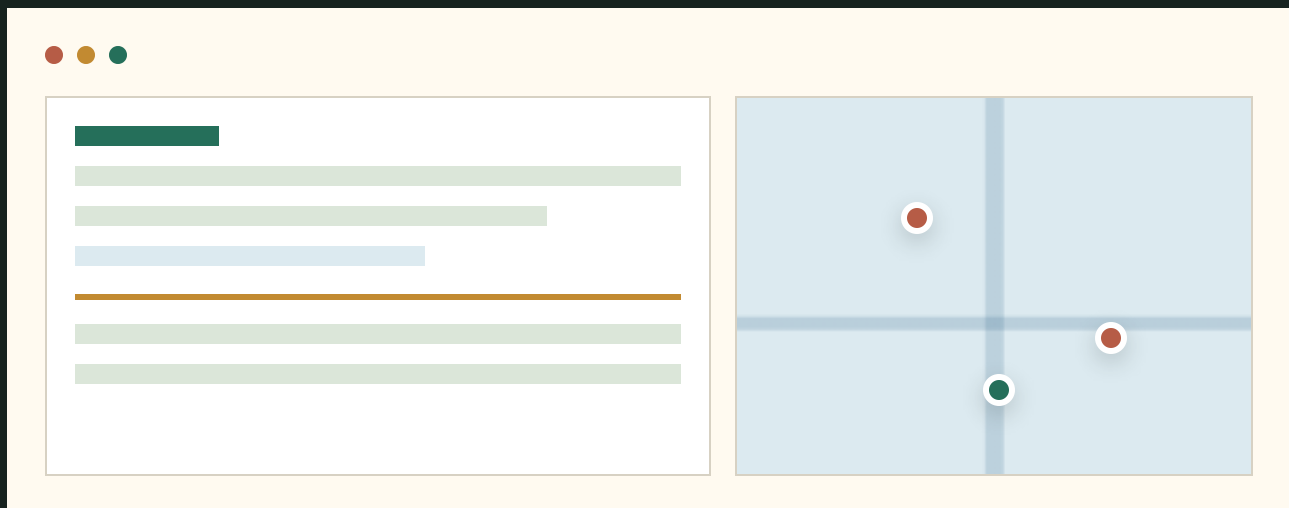

 WHERE THE FIRST SEASON LANDED

The first season ended with a concrete demo, not just a concept.

The end-of-season presentation showed the core shape of the portal already exists across public, partner, and admin workflows. The second season starts from that foundation and asks what needs to be true for stakeholder use.

01

Public listings

Search, filters, map view, listing details, and server-first data loading.

02

Partner tools

Listing authoring, drafts, image uploads, and a My Listings workspace.

03

Admin controls

Invites, user management, roles, and configurable listing fields.

04

Real backend

Next.js, Postgres, Drizzle migrations, shared schemas, auth, tests, and CI hooks.

FIRST-SEASON OUTPUT							02 / 08	

THE SECOND-SEASON PROBLEM

A working prototype is not the same as a usable service.

The next season should close the gap between code that exists and software a stakeholder can trust with real users, content, and operations.

01 Stakeholder fit is still unproven

Sean will circulate the existing code/demo to gather feedback from the stakeholder side.

02 Launch readiness needs focused work

Deployment, onboarding, content setup, performance, QA, and documentation need a deliberate pass.

03 The backlog now has product direction

Open issues point to search quality, alerts, no-code resources, accessibility fields, and performance.

SECOND-SEASON OPERATING MODEL

Make stakeholder feedback the engine of the season.

Instead of guessing what polish means, we run a tight loop from Sean's stakeholder review back into prioritized implementation.

01

Share

Sean sends the current portal to stakeholders for first-pass review.

02

Collect

Capture workflow gaps, confusing language, missing fields, and trust blockers.

03

Translate

Turn feedback into GitHub issues with acceptance criteria and screenshots.

04**Ship**

Volunteer pairs take small slices through design, implementation, and review.

05**Validate**

Replay the stakeholder workflow and decide what is launch-blocking.

FEEDBACK LOOP

04 / 08

BACKLOG EVIDENCE

The open issues already describe a practical second-season roadmap.

Launch readiness

core

Search quality

#29

Alerts + saves

#27 #8

No-code resources

#28

Accessibility fields

#24

Likely second-season feature themes

- Graded preferences: required vs. preferred filters, relevance metadata, and better result ranking.
- Listing alerts and saved searches: help users act when suitable housing appears.
- No-code resources: let admins maintain public support content without a developer deploy.
- Accessibility and amenity audit: confirm the fields stakeholders actually need.
- Performance and polish: lazy-load heavy filter UI and fix feedback-driven usability gaps.

GITHUB ISSUES: #226, #39, #38, #37, #36, #35, #34, #33, #29, #28, #27, #24, #8								05 / 08	

 VOLUNTEER SHAPE

The second season has room for different kinds of contributors.

Product / UX

Turn feedback into clear slices

- Stakeholder interview notes
- Issue triage
- Acceptance criteria

Frontend

Make workflows usable

- Search UX
- Listing authoring
- Admin screens

Backend

Finish durable product logic

- Alerts
- Saved searches
- Resource CRUD

DevOps / QA**Get it deployable**

- Environment setup
- Regression tests
- Launch checklist

Content**Prepare handoff material**

- Admin docs
- Seed content
- Training notes

 16-WEEK PLAN

A 16-week season can move from review to pilot readiness.

Weeks 1-3

Baseline and deploy path

Run the app cleanly, document setup, identify launch blockers, and prepare a stakeholder demo environment.

Weeks 4-6

Feedback intake

Sean gathers review input; volunteers convert it into scoped fixes and prioritize what matters for use.

Weeks 7-12

Build the highest-value gaps

Ship selected search, alerts, resources, accessibility, performance, and polish workstreams.

Weeks 13-16

UAT and handoff

Test real workflows, finalize docs, seed content, and decide what is ready for stakeholder use.

PROPOSED 16-WEEK CADENCE

07 / 08

 THE PROPOSAL

Let's make the second season the launch-readiness push.

The goal is not to add features endlessly. The goal is to make the portal useful enough for the stakeholder to evaluate in practice and put into service with confidence.

Keep the project going

Frame the work around stakeholder validation, deployment readiness, and a pilot-ready handoff.

Bring in the right mix

Frontend, backend, QA, product, content, and documentation contributors can all move the portal forward.

Follow the feedback

Use Sean's stakeholder input as the source of truth for what gets fixed, polished, or deferred.

Aim for a clear finish line

A deployable portal, validated core workflows, and a stakeholder handoff plan by the end of the season.

SECOND-SEASON PITCH

08 / 08
